
ID		Task Name	Duration	Start	Finish	% Complete	Apr 12, '20					Apr 19, '20			Apr 26, '20				May 3, '20			M	May 10,		
	e						Т	S	M	W	F	S	Т	Т	S	Μ	W	F	S	T	Т	S	M		
1																									
2		Overall Plan for Electrical Resistence Testing	34 days	Mon 4/13/20	Thu 5/28/20	14%			,																
3		Ardager Residence Blocks 1,2,3/2F TCO office	6 days	Mon 4/13/20	Mon 4/20/20	75%			, 			-	I												
4		For Inspection/Test of Block 1 required 6 work days	6 days	Mon 4/13/20	Mon 4/20/20	75%			-		-														
5		Ardager Residence Block 1, Apartments Inspection/Test	8 days	Tue 4/21/20	Thu 4/30/20	0%									_		ii								
6		For Inspection/Test of Block 1 required 8 work days	8 days	Tue 4/21/20	Thu 4/30/20	0%								-			-								
7		Ardager Residence Block 2, Apartments Inspection/Test	11 days	Mon 5/4/20	Mon 5/18/20	0%																	_		
8		For Inspection/Test of Block 2 required 10 work days	11 days	Mon 5/4/20	Mon 5/18/20	0%																	-		
9		Ardager Residence Block 3, Apartments Inspection/Test	8 days	Tue 5/19/20	Thu 5/28/20	0%																			
10		For Inspection/Test of Block 3 required 8 work days	8 days	Tue 5/19/20	Thu 5/28/20	0%																			

	Task		Project Summary	Inactive Milestone	\$	Manual Summary Rollup			
Project: Project1	Split		External Tasks	Inactive Summary	$\bigtriangledown \qquad \bigtriangledown$	Manual Summary			
Date: Fri 4/17/20	Milestone	♦	External Milestone	Manual Task]	Start-only	C		
	Summary	~	Inactive Task	Duration-only		Finish-only	2		
				Page 1					

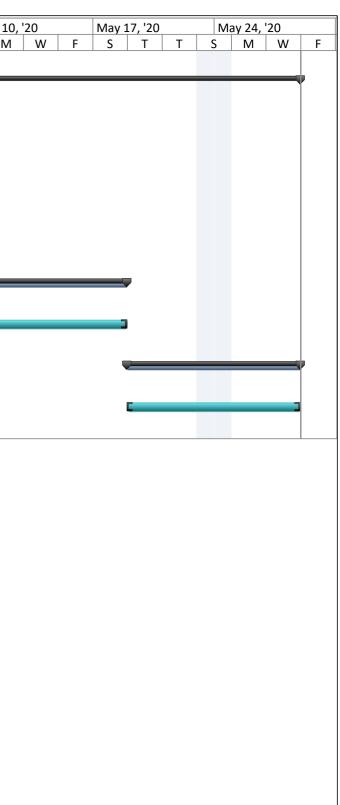

Deadline Progress
